

Consultant Report Amendment: Tree Program Financial Projection as of 5/30/19



No. of Trees as of 7/1/18		443
Less: Trees removed 7/1/18-5/30/19		(697)
Plus: Additional trees added 7/1/18-5/30/19		334
Less: Cancellations 7/1/18-5/30/19		(72)
No. of Trees as of 5/30/19	-	8
Est. remaining cost as of 7/1/18	\$	1,346,975
Less: Trees removed 7/1/18-5/30/19		(1,894,515)
Plus: Additional trees added 7/1/18-5/30/19		836,915
Less: Cancellations 7/1/18-5/30/19		(184,910)
Less: Discounts 7/1/18-5/30/19		(52,300)
Est. Remaining Cost as of 5/30/19	\$	52,165
FY19 Budget	\$	2,000,000
Less: Amt. Billed by S.P. McClenahan as of 5/30/19		(1,842,215)
Less: Amt. Billed by Kielty Arborist as of 5/30/19		(21,000)
Less: Other costs (letterhead) as of 5/30/19		(780)
Remaining FY19 Budget	\$	136,005

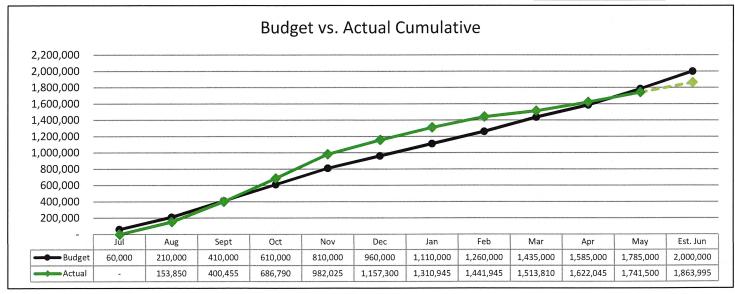

Note 1: "Est. Jun" only includes what has been billed as of 6/10/19, more invoices from McClenahan & Kielty are expected at the end of the month
